

## Garretson Elementary 2017-2018 Phase 2

### Weekly Construction Progress Update, Week Ending August 31<sup>th</sup>, 2018

Billing through 8/31/18 reflects that the project is 94% Contract completion date: October 2018

#### This week's activities

- Painted interior walls / doors and frames at building D
- Finish stucco color coat at building D and C
- Start T-Bar building D / Ceramic tile finishing building D
- Building C drywall taping

#### Next week's activities

- Paint exterior building D
- Casework delivery building D
- Continuing taping drywall at building C.
- Roofing continues / Sheetmetal Building C starting




Building D color coat



Building D T-Bar grid, doors painted



Landscaping in Progress

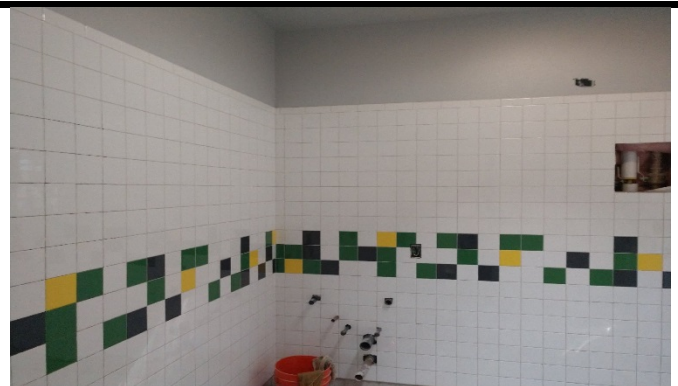

Ceramic Tile in Progress
