

## Garretson Elementary 2017-2018 Phase 2

### Weekly Construction Progress Update, Week Ending July 6<sup>th</sup>, 2018


Billing through 6/30/18 reflects that the project is 85% Contract completion date: October 2018

#### This week's activities

- Continue Framing Walls @ Building C
- Setting light poles in parking lot
- finished tack Board building 3
- Setting up Concrete site work throught
- MEP Trades Continue in building D

#### Next week's activities

- Starting T-Bar ceilings in Building 3
- Continue Framing
- Curb and gutter crew starting

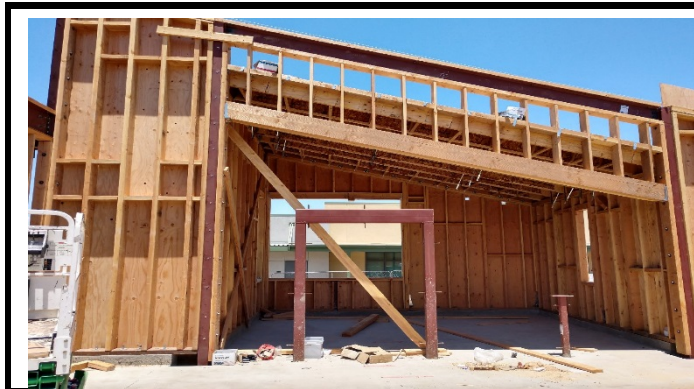

Framing at Building C



Concrete crew setting up Forms



HVAC rough in Building D



Play structure Base
