

## Garretson Elementary 2017-2018 Phase 2

### Weekly Construction Progress Update, Week Ending November 2, 2018


Billing through 10/31/18 reflects that the project is 99% Contract completion date: October 2018

#### This week's activities

- Finished Landscaping
- Data, Fire alarm and Security Finishing up this week
- Finished Carpet

#### Next week's activities

- Testing Data, PA., Fire alarm and security
- Clean up
- Punchlist walks next week

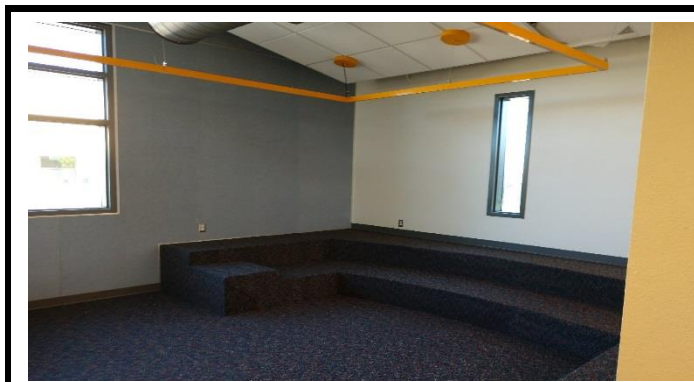

**Media Center, Story Room**



**Media Center, Display case**



**Building C, Landscaping**



**Building C, Landscaping**
