

Norco Elementary 2017-2018 Phase 2

Weekly Construction Progress Update, Week Ending May 11, 2018

Billing through 4/30/18 reflects that the project is 81% Contract completion date: August 2018

This week's activities:


- Demolition of concrete at portables.
- Removed electrical, data, and fire alarm devices inside portables.
- Disconnect underground & overhead power to portables.
- Removal of portables.

Next week's activities

- Begin demolition on old Library.
- Begin demolition of concrete at new Lunch Shelter.
- Begin demolition of concrete at fire lane.



Demolition of concrete ramp

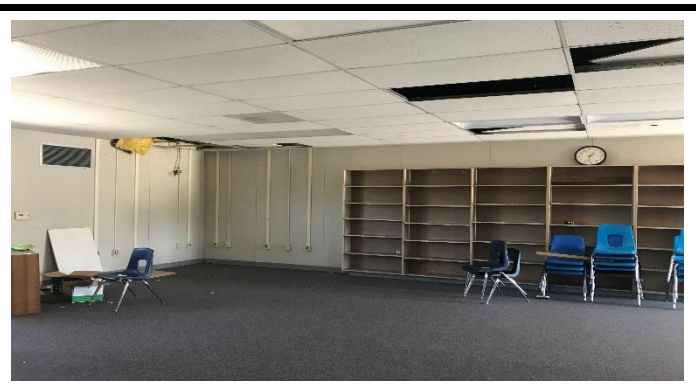

Portable devices



Removal of power



Removal of portables
